


WORKING HOURS

TRAFFIC CONTROL PLAN
2792J - VARIOUS LOCATIONS PAVEMENT RENOVATION NO. 37 AND SEWER REPLACEMENT
CURB RAMP WORK PLAN - 18TH ST FROM ARKANSAS ST TO MISSOURI ST

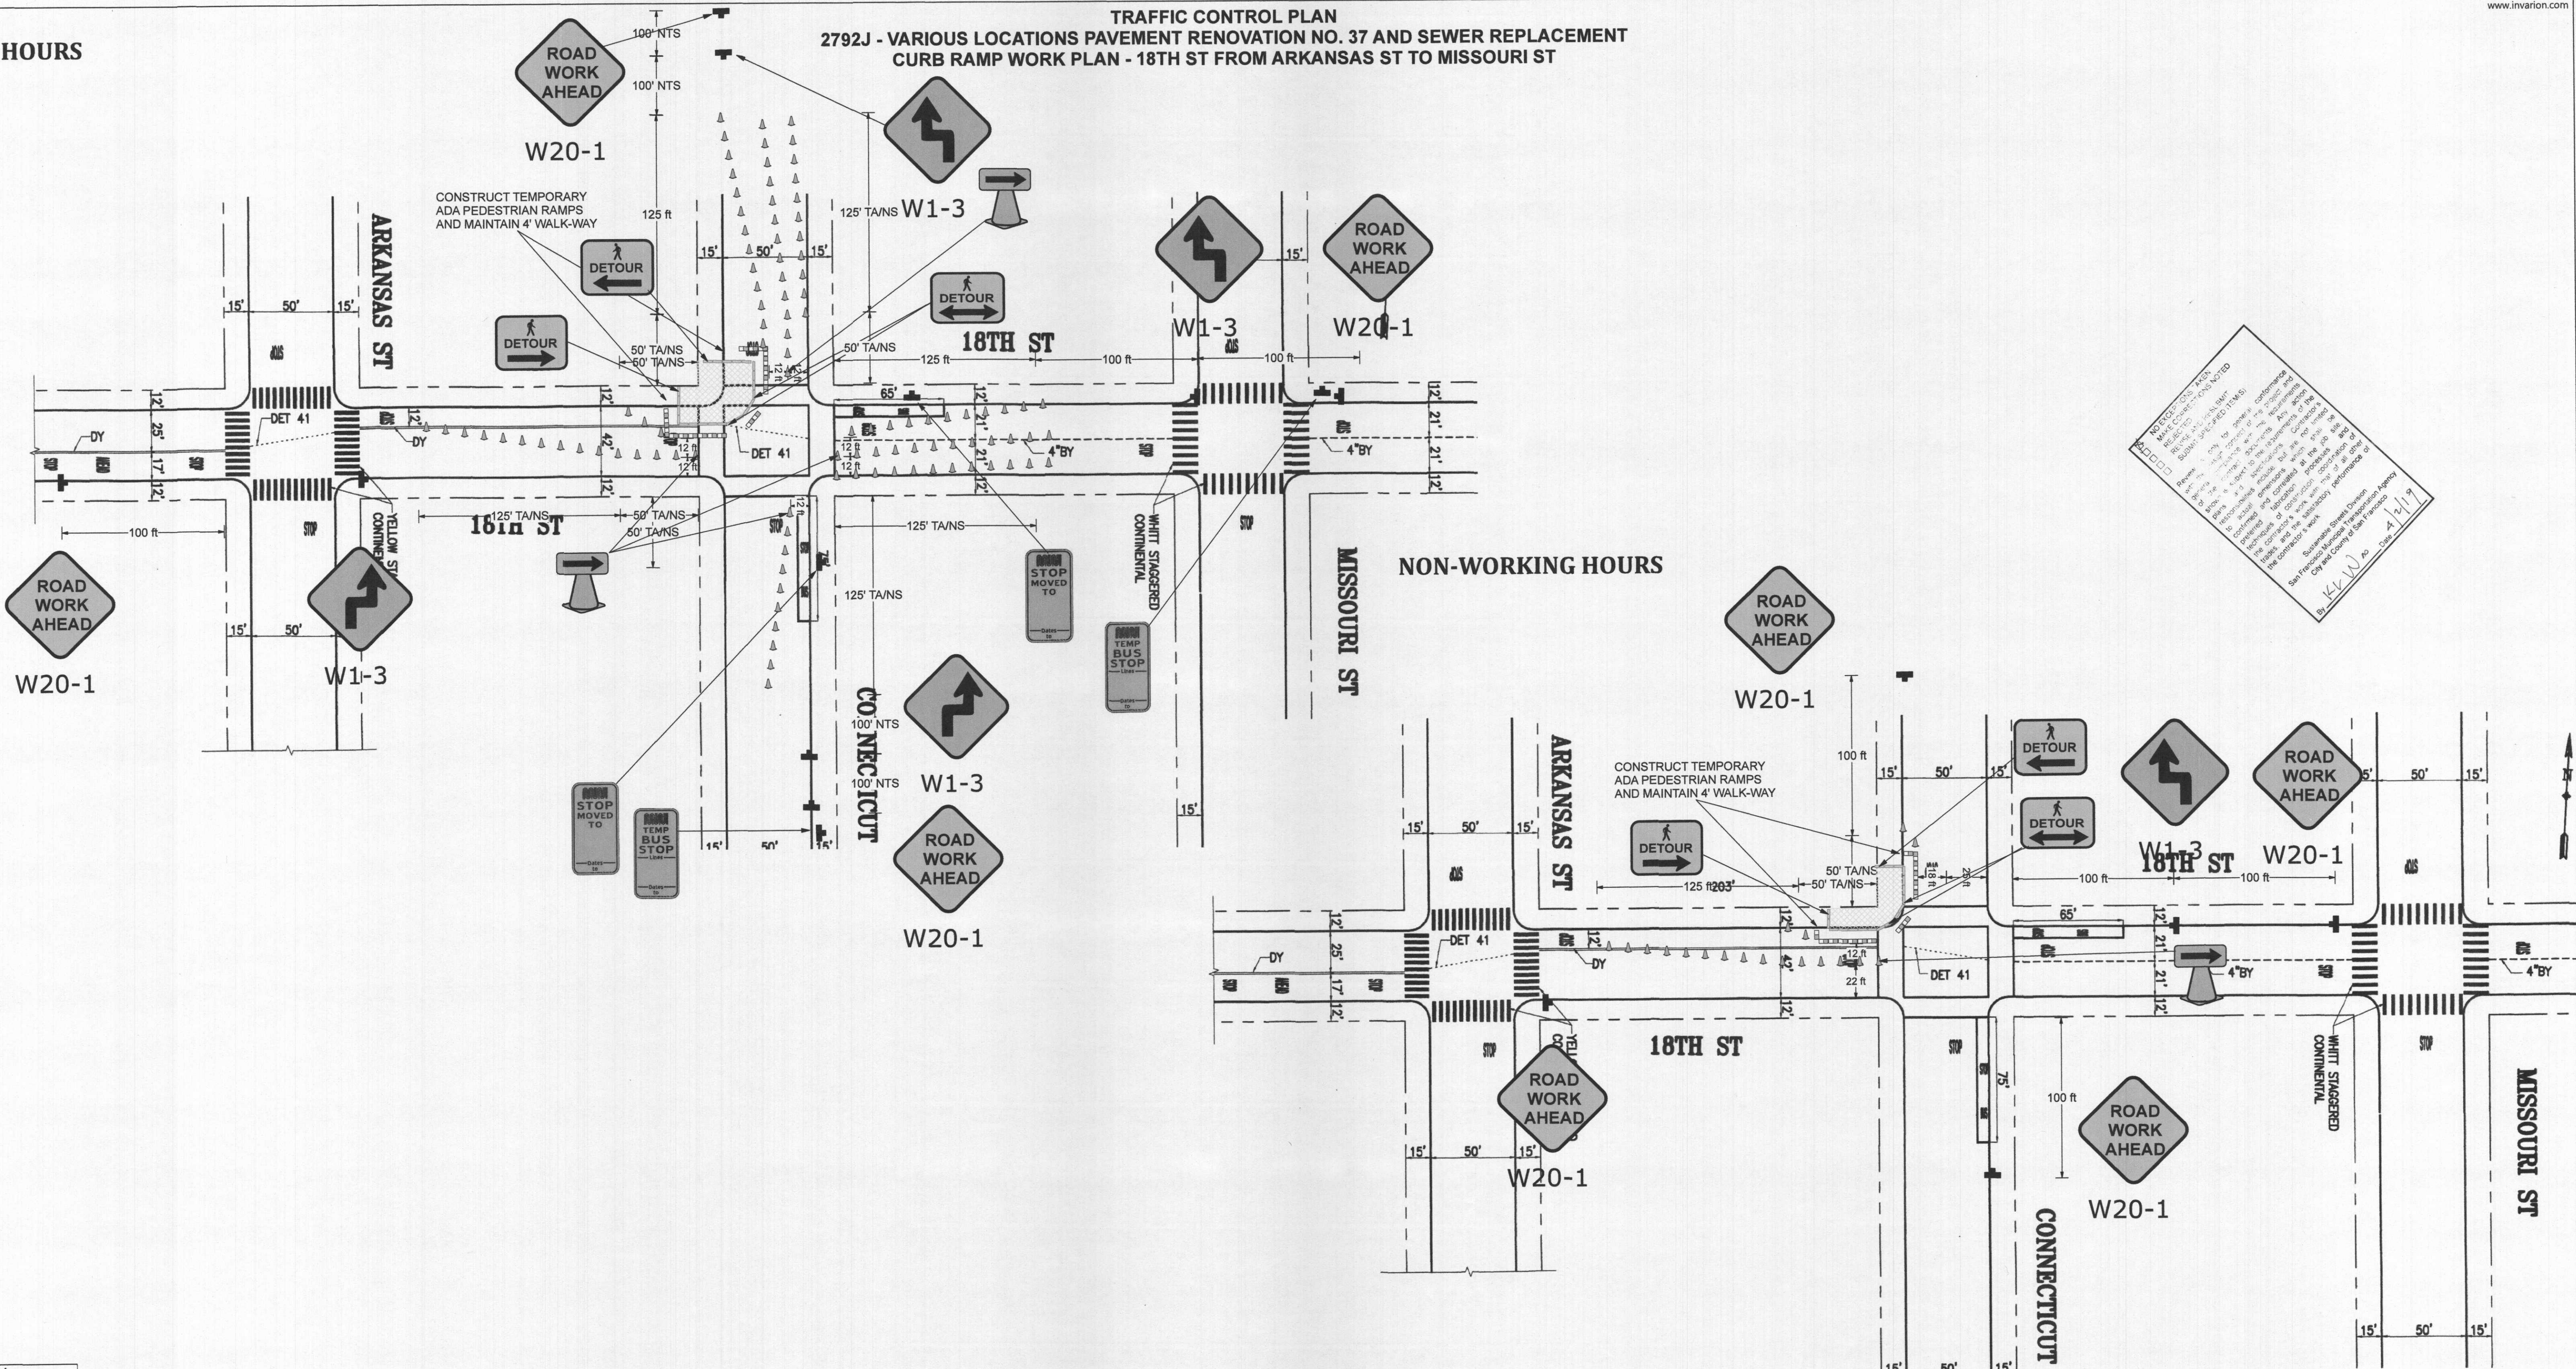

Legend

- Type III Barricade
- 28" Traffic Cone
- Work Area
- Sign and Stand
- Direction of Travel
- Type III Barricade (Plain View)
- Water Filled Barrier
- NTS Not To Scale
- T/ANS Tow-Away/No Stopping
- Police Officer
- Flagger
- Type I Barricade
- Work Truck
- Pipe to be installed
- Existing Utility
- Flashing Beacon



STREET	TIME	NORTHBOUND	SOUTHBOUND	EASTBOUND	WESTBOUND
During Curb Ramp and Sidewalk Construction					
18th St. at Connecticut St.	9AM - 4PM (M-F) 8AM - 6PM (S/S) At Other Times	-	-	1@12' 1@12' Full Roadway	1@12' 1@12' Full Roadway
Kansas, Arkansas, Connecticut,	8AM - 6PM At Other Times	1@12' Full Roadway	1@12' Full Roadway	-	-



3450 3RD ST #3G
SAN FRANCISCO, CA 94124
415-206-1700 PHONE
415-206-1711 FAX
INFO@CMCTRAFFIC.COM

LICENSE NO. 792059
CLASS A, 31, C21
WBE/SBE/LBE/DBE CERTIFIED
WWW.CMCTRAFFIC.COM

Date: 03/05/2019 Author: RC/PM Project: 2792J
CLIENT: PRECISION Owner: SFPDPW Location: SAN FRANCISCO
TCP: 094 CMC Job #: 1812

- Comments:**
- 1) WORK HOURS:
 - 2) CONTRACTOR TO VERIFY EXISTING STRIPING IS ACCURATE PRIOR TO START OF WORK.
 - 3) ALL TRAFFIC CONTROL SHALL CONFORM TO THE LATEST EDITION OF CA MUTCD.
 - 4) ALL TRAFFIC CONTROL DEVICES SHALL BE RETROREFLECTIVE IF SETUP DURING HOURS OF DARKNESS.
 - 5) THE CONTRACTOR SHALL BE ALLOWED TO WORK AT A MAXIMUM OF THREE INTERSECTIONS AT ANY TIME IF THERE ARE MULTIPLE CURB RAMP TO BE CONSTRUCTED ALONG A STREET, EXCEPT AS OTHERWISE NOTED IN SPECIFICATIONS.
 - 6) NO CROSSWALK SHALL BE ALLOWED TO BE CLOSED DURING CURB RAMP WORK EXCEPT DURING DEMOLITION OF CURB RAMP IN WHICH CONTRACTOR MAY CLOSE ONLY ONE CROSSWALK AT A TIME AND PROVIDE TWO FLAGGERS TO GUIDE PEDESTRIANS TO THE OPEN CROSSWALK.
 - 7) MAINTAIN LOCAL ACCESS TO BUSINESSES AND RESIDENTS AT ALL TIME.
